DIGITAL LEGACY MANAGER

A Secure System for Managing and Transferring Digital Assets

Assignment 2 – Agile / Scrum Project Management Using Jira

Team Members

Team Member	Roll Number
S. Mukundhan	CB.EN.U4CCE24033
VISHAL ADITYA RAMESH	CB.EN.U4CCE24065
K. Bharath Kumar	CB.EN.U4CCE24013

Project	Digital Legacy Manager
Methodology	Scrum
Tool	Jira
Evidence period	August–October 2026

Prepared from the team's Jira evidence and project definition. Screenshots are presented as evidence of backlog structure, user-story decomposition, Sprint planning, release planning, progress tracking and Scrum-board execution.

1. Project Overview & Scope

Project Goal. Digital Legacy Manager is intended to provide a secure way to organize, protect and transfer a person's digital assets to authorized beneficiaries after death or incapacity. The project focuses on secure account management, asset protection, beneficiary management, legal verification and controlled release.

Problem Statement. Digital assets may contain important documents and sensitive information. Without a structured mechanism for ownership, verification and controlled transfer, beneficiaries may be unable to receive assets while unauthorized or invalid requests may create security and legal risks.

Target Users.

- Ordinary users who manage their digital legacy.
- Beneficiaries who request and receive released assets.
- Verification authorities who validate death certificates.
- Legal executors who verify documents and approve or reject release requests.
- Administrators who manage accounts and monitor audit activity.

Core Functional Scope.

- Registration, login, profile update and logout
- Digital-asset creation, document upload, encryption and viewing
- Digital-will creation, beneficiary assignment and transfer conditions
- Beneficiary requests and death-certificate verification
- Legal-document verification and executor approval/rejection
- Released-asset access and release notifications
- Account administration, suspension/restoration and audit logging

The Jira backlog converts this scope into a traceable set of Epics, User Stories and implementation/testing subtasks.

2. Jira Project Structure

The project is organized into **5 Epics**, **21 User Stories** and a larger set of implementation/testing subtasks. The Product Backlog contains **84 story points** in total.

Epic	Module	Points	Scope
Epic 1	User Authentication & Account Management	10	Registration, login, profile update and logout.
Epic 2	Digital Asset Management	21	Adding, uploading, encrypting and viewing digital assets.
Epic 3	Digital Will & Beneficiary Management	16	Creating/updating the digital will, assigning beneficiaries and defining transfer conditions.
Epic 4	Verification & Asset Release	23	Beneficiary requests, death-certificate verification, legal-document verification, executor decisions and released-asset access.
Epic 5	Notifications, Administration & Audit	14	Release notifications, account administration, suspension/restoration and audit logging.

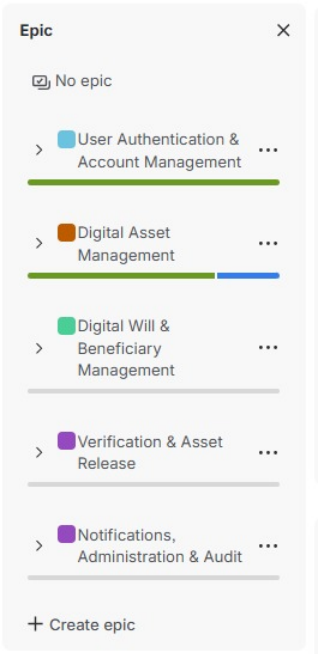


Figure 1. Jira Epic panel showing the five project epics.

2.1 Team Responsibilities & Work Ownership

The Jira evidence shows work distributed across the three team members, with functional ownership reflected through assignees and issue organization.

Member	Observed Jira responsibility	Primary functional area
VISHAL ADITYA RAMESH	Story/subtask ownership; Sprint 1 implementation	Authentication, account management and digital assets
S. Mukundhan	Story ownership for digital-will module	Digital will and beneficiary management
K. Bharath Kumar	Story ownership for release/admin module	Verification, asset release, notifications and administration

Jira fields such as **Parent Epic, Sprint, Priority, Labels and Assignee** provide traceability from a requirement to its planned implementation.

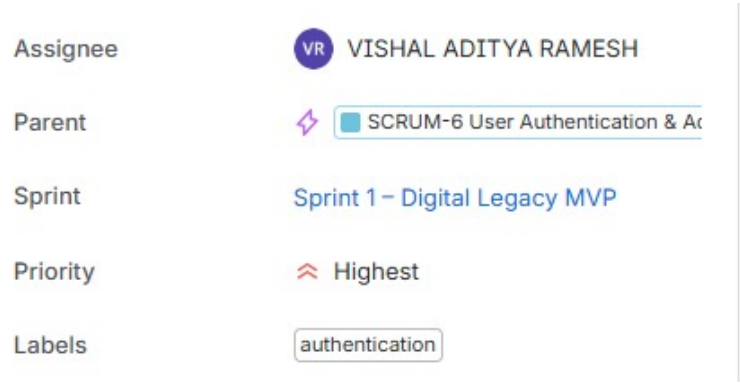


Figure 2. Issue-level evidence showing assignee, parent epic, Sprint, priority and label.

2.2 Product Backlog & User-Story Decomposition

The Product Backlog contains 21 User Stories covering all five Epics. Story points range from 2 to 8, allowing the team to estimate relative effort and order the work according to functional dependency and importance.

Product backlog 21 issues


#	Issue		Epic	Type	Priority	Story points
1	SCRUM-12	As a user, I want to register an account, so that I can securely use the Digital Legacy Manager.	User Authentic...	Story	High	3
2	SCRUM-13	As a user, I want to log in securely, so that I can access my digital assets and account.	User Authentic...	Story	High	3
3	SCRUM-14	As a user, I want to update my profile information, so that my account details remain accurate.	User Authentic...	Story	High	2
4	SCRUM-15	As a user, I want to securely log out of my account, so that unauthorized users cannot access my account.	User Authentic...	Story	High	2
5	SCRUM-16	As a user, I want to add digital assets, so that I can organize my important digital information.	Digital Asset M...	Story	High	5
6	SCRUM-17	As a user, I want to upload legal documents, so that important documents can be securely stored.	Digital Asset M...	Story	High	5
7	SCRUM-18	As a user, I want my digital assets to be encrypted, so that sensitive information remains protected.	Digital Asset M...	Story	High	8
8	SCRUM-19	As a user, I want to view my stored digital assets, so that I can manage the information I have saved.	Digital Asset M...	Story	High	3
9	SCRUM-20	As a user, I want to create a digital will, so that I can specify how my digital assets should be transferred.	Digital Will & B...	Story	High	5
10	SCRUM-21	As a user, I want to assign beneficiaries, so that my digital assets can be transferred to authorized people.	Digital Will & B...	Story	High	3
11	SCRUM-22	As a user, I want to define conditions for asset transfer, so that assets are released according to my wishes.	Digital Will & B...	Story	High	5
12	SCRUM-23	As a user, I want to update my digital will, so that my asset-transfer instructions remain current.	Digital Will & B...	Story	High	3
13	SCRUM-24	As a beneficiary, I want to request access to digital assets, so that I can receive assets assigned to me.	Verification & A...	Story	Medium	5
14	SCRUM-25	As a verification authority, I want to verify the death certificate, so that only valid requests proceed.	Verification & A...	Story	Medium	5
15	SCRUM-26	As a legal executor, I want to verify legal documents, so that asset-release requests can be legally validated.	Verification & A...	Story	Medium	5
16	SCRUM-27	As a legal executor, I want to approve or reject asset-release requests, so that assets are released only after proper verification.	Verification & A...	Story	High	3
17	SCRUM-28	As a beneficiary, I want to view and download released assets, so that I can securely access assets assigned to me.	Verification & A...	Story	High	3
19	SCRUM-29	As a beneficiary, I want to receive asset-release notifications, so that I know when my requested assets are available.	Notifications, A...	Story	High	3
20	SCRUM-30	As an administrator, I want to manage user accounts, so that I can maintain the security of the system.	Notifications, A...	Story	High	3
21	SCRUM-31	As an administrator, I want to suspend or restore accounts, so that inappropriate or compromised accounts can be controlled.	Notifications, A...	Story	High	3
21	SCRUM-32	As an administrator, I want to view audit logs, so that important system activities can be monitored.	Notifications, A...	Story	High	5

Figure 3. Jira Product Backlog showing the 21 User Stories, Epic relationships, priorities and story points.

Total backlog estimate: 84 story points. The backlog ordering reflects a dependency-aware sequence: secure access first, asset management next, digital-will functionality after the asset foundation, and verification/release and administrative capabilities later.

3.1 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

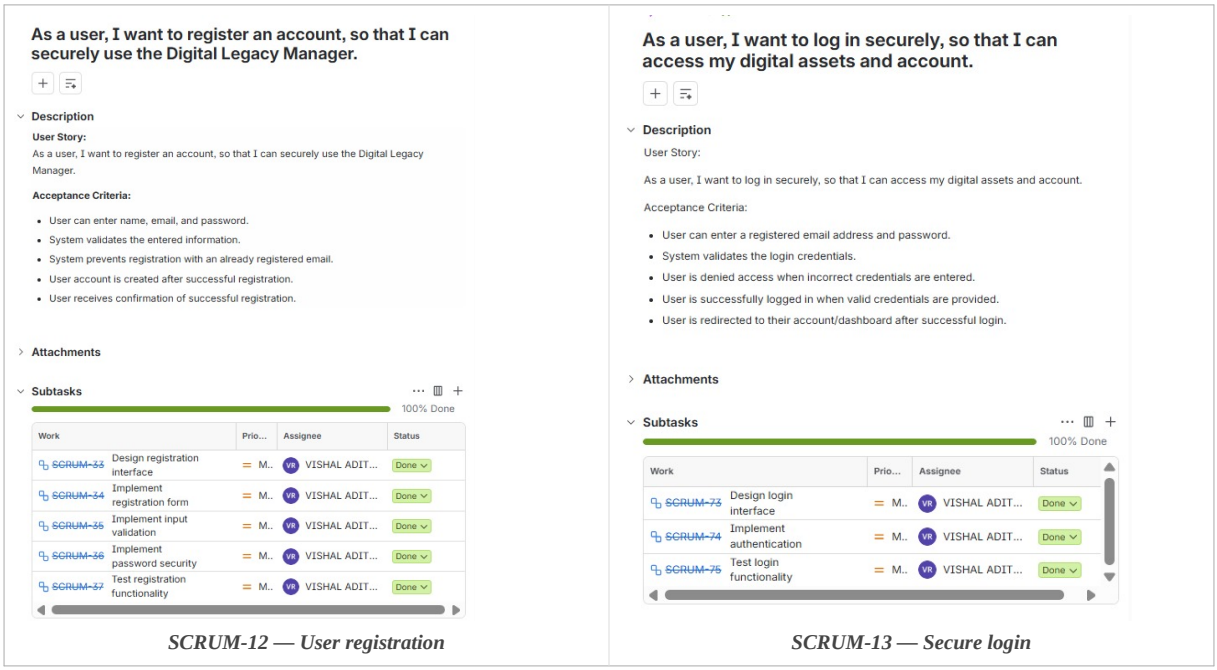


SCRUM-12 — User registration

SCRUM-13 — Secure login

Epic 1 — User Authentication & Account Management: registration, login, profile maintenance and logout.

3.2 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

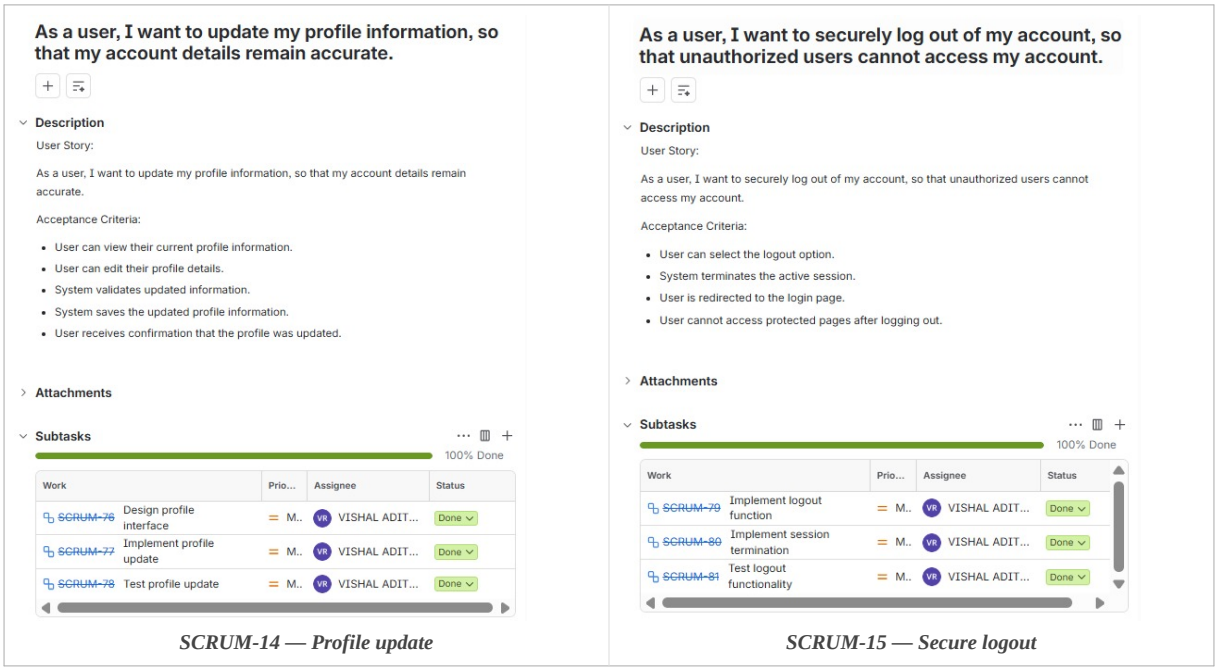


SCRUM-14 — Profile update

SCRUM-15 — Secure logout

3.3 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

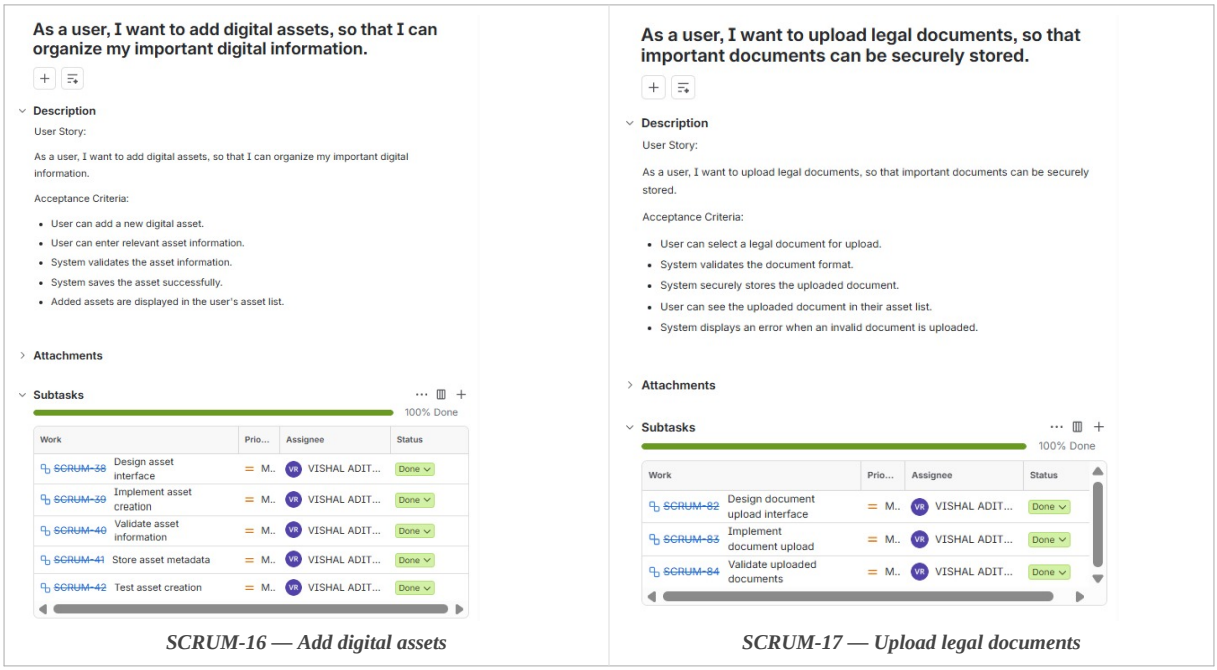


SCRUM-16 — Add digital assets

SCRUM-17 — Upload legal documents

Epic 2 — Digital Asset Management: asset creation, legal-document upload, encryption and viewing.

3.4 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

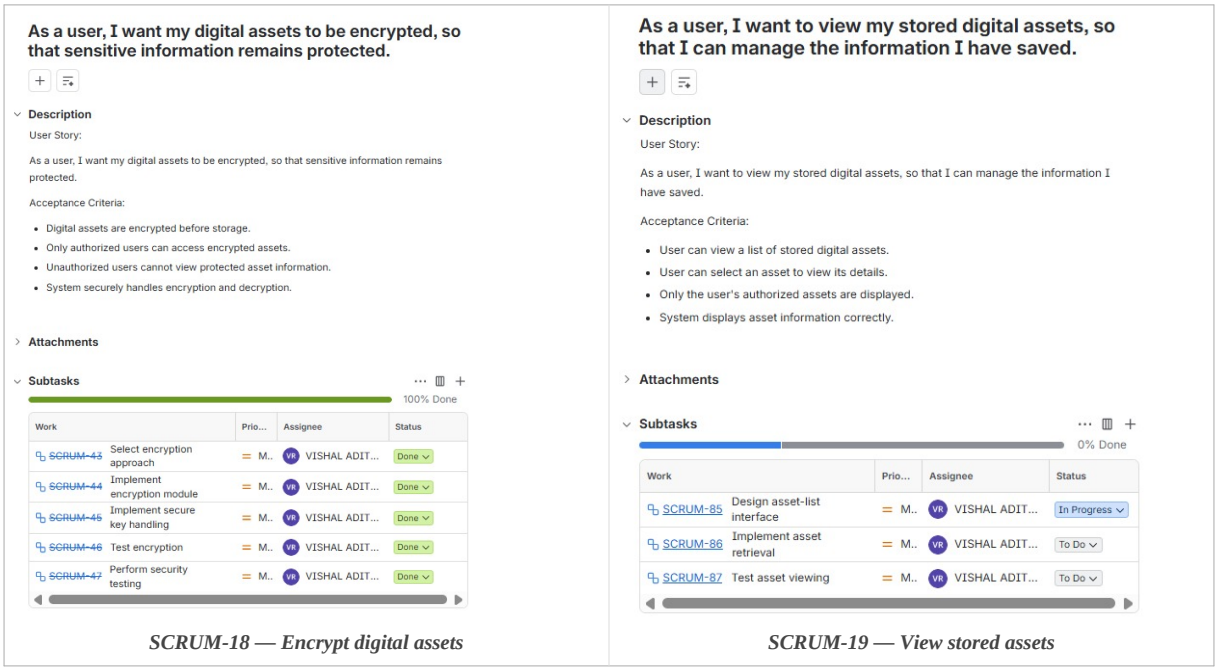


SCRUM-18 — Encrypt digital assets

SCRUM-19 — View stored assets

3.5 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

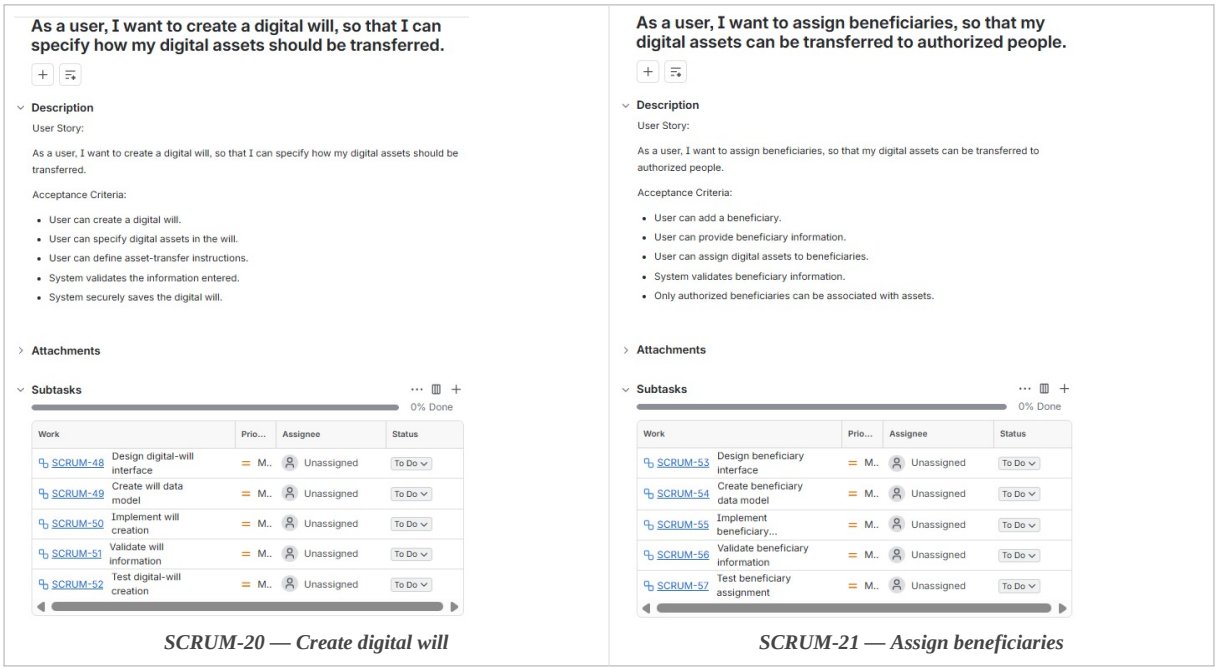


SCRUM-20 — Create digital will

SCRUM-21 — Assign beneficiaries

Epic 3 — Digital Will & Beneficiary Management: digital-will creation, beneficiaries, conditions and updates.

3.6 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

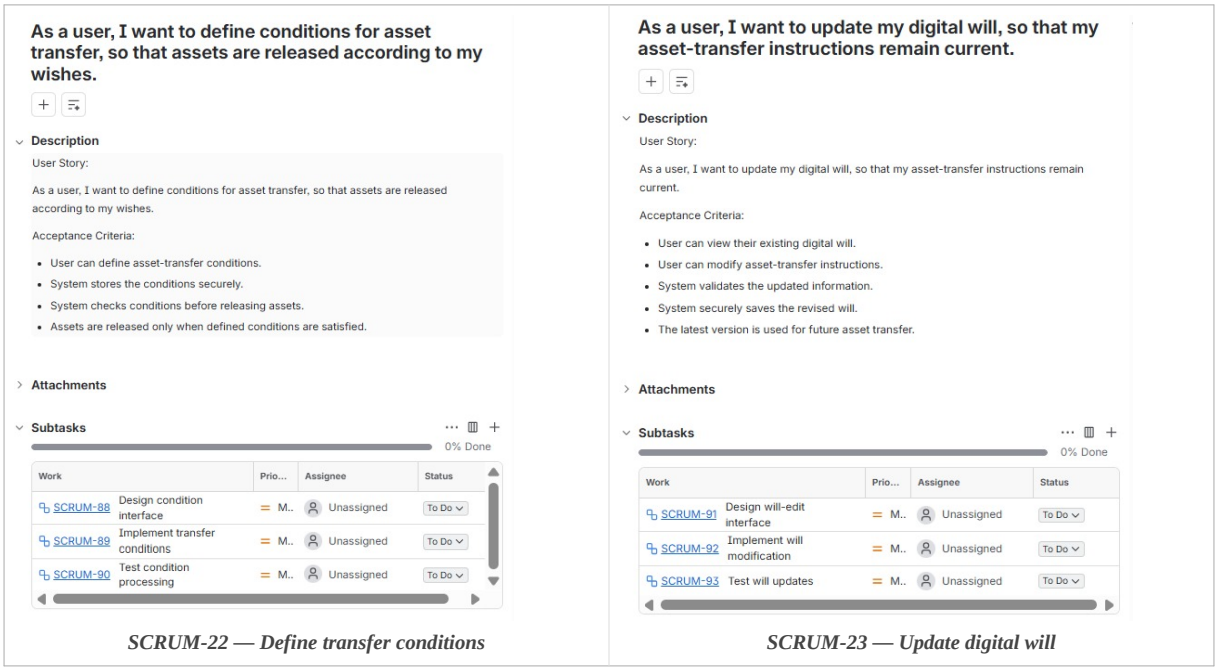


SCRUM-22 — Define transfer conditions

SCRUM-23 — Update digital will

3.7 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

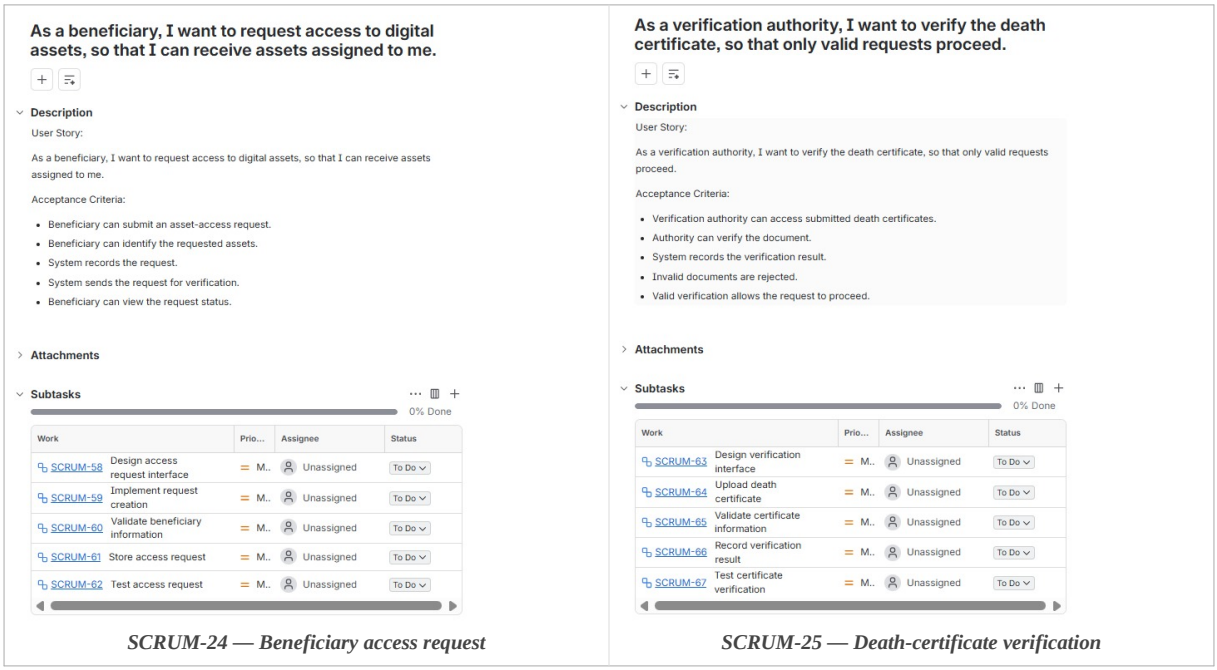


SCRUM-24 — Beneficiary access request

SCRUM-25 — Death-certificate verification


Epic 4 — Verification & Asset Release: beneficiary requests, certificate/document verification, executor decision and released-asset access.

3.8 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

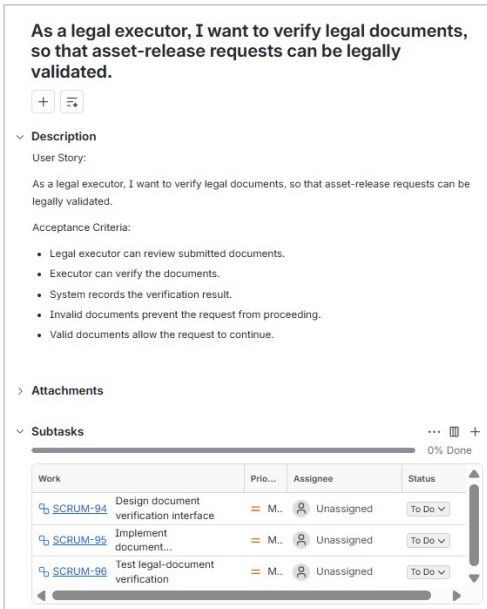


SCRUM-26 — Legal-document verification

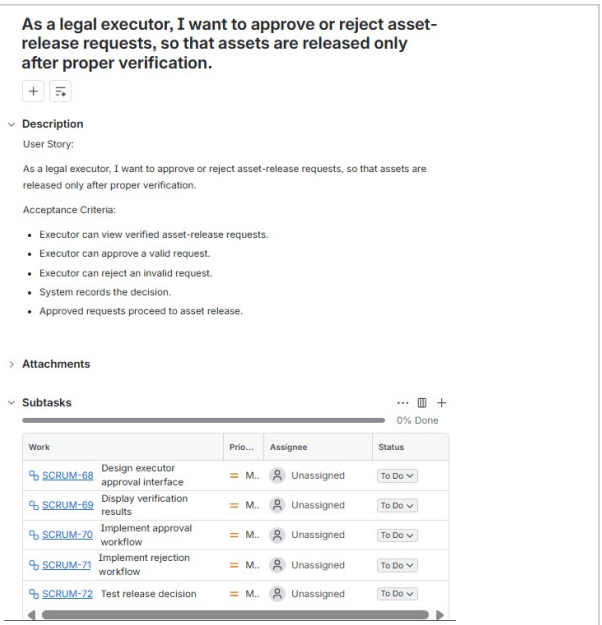

SCRUM-27 — Executor approval/rejection

3.9 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

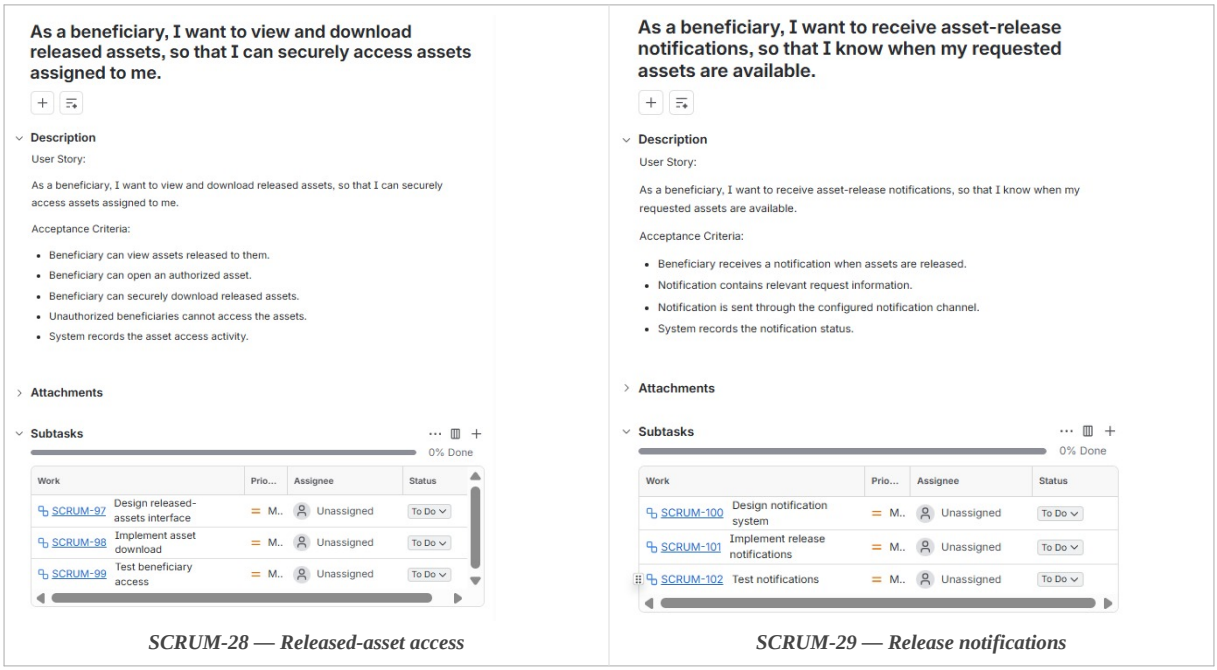


SCRUM-28 — Released-asset access


SCRUM-29 — Release notifications

3.10 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

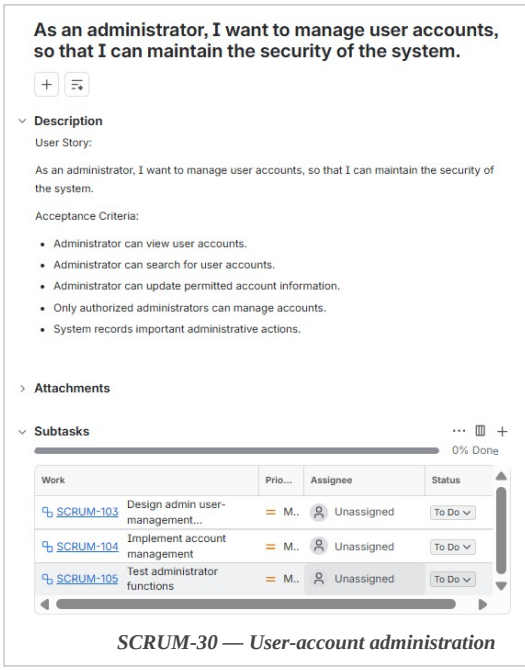

SCRUM-30 — User-account administration

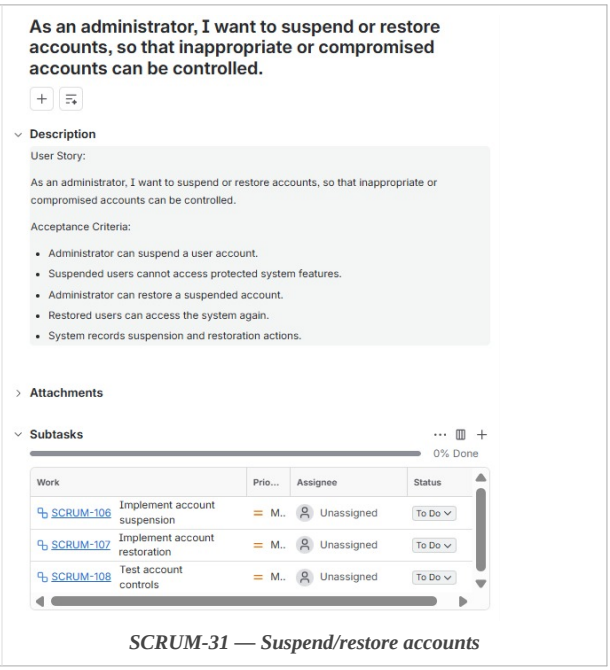


SCRUM-31 — Suspend/restore accounts

Epic 5 — Notifications, Administration & Audit: notifications, account administration, suspension/restoration and audit logs.

3.11 User Story Evidence

The following Jira issue screenshots demonstrate the standard Scrum User Story format, acceptance criteria and decomposition into subtasks. The evidence is grouped by the project's functional sequence.

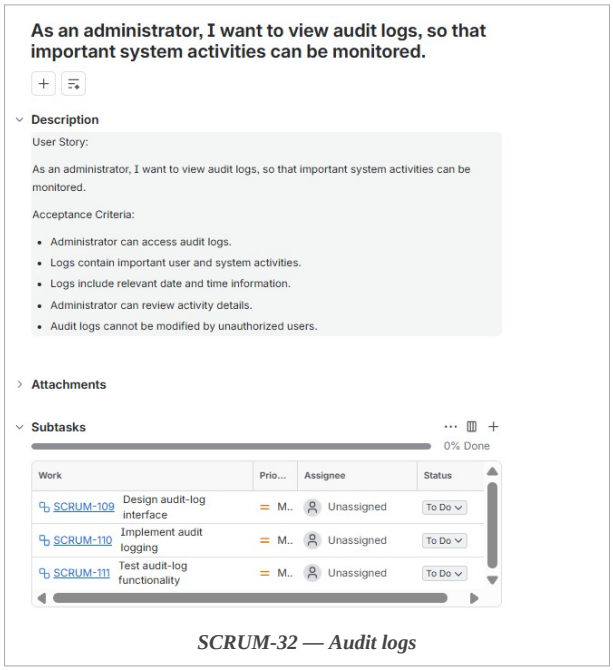

SCRUM-32 — Audit logs

4. Sprint Planning & Backlog Allocation

The backlog is divided into three time-boxed Sprints. The allocation follows the project's dependency chain and separates core functionality, digital-will enhancements and verification/release/testing work.

Sprint	Dates	Stories	Points	Goal
Sprint 1 – Digital Legacy MVP	26 Aug – 7 Sep	SCRUM-12 to 15, SCRUM-18 to 19	21	Implement the core secure account and digital-asset foundation.
Sprint 2 – Enhancements	7 Sep – 21 Sep	SCRUM-20 to 23	16	Complete digital-will and beneficiary functionality.
Sprint 3 – Testing	21 Sep – 5 Oct	SCRUM-24 to 32	37	Test verification, release, notifications and administration functionality.

Two stories — SCRUM-16 and SCRUM-17 — are visible in the Product Backlog but are not part of the three displayed Sprint allocations. This should be treated as a scope item to review before execution.

4.1 Sprint Boards

Sprint 1 – Digital Legacy MVP. The board evidence shows six work items. The core authentication stories and encryption work are marked Done, while the stored-assets story is In Progress.

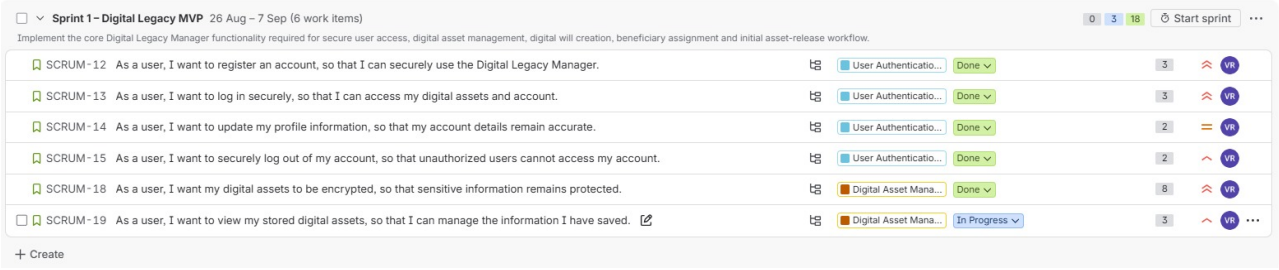


Figure 4. Sprint 1 planning view and goal.

Sprint 2 – Enhancements. Four digital-will/beneficiary stories are planned for the second increment, with a 16-point scope.




Figure 5. Sprint 2 planning view and goal.

4.2 Sprint 3 – Testing

Sprint 3 contains nine stories totaling 37 points. Its stated goal is to test the Digital Legacy Manager, fix functional and security issues, and prepare the system for final release. The planned work covers beneficiary requests, verification, executor decisions, released-asset access, notifications and administration.


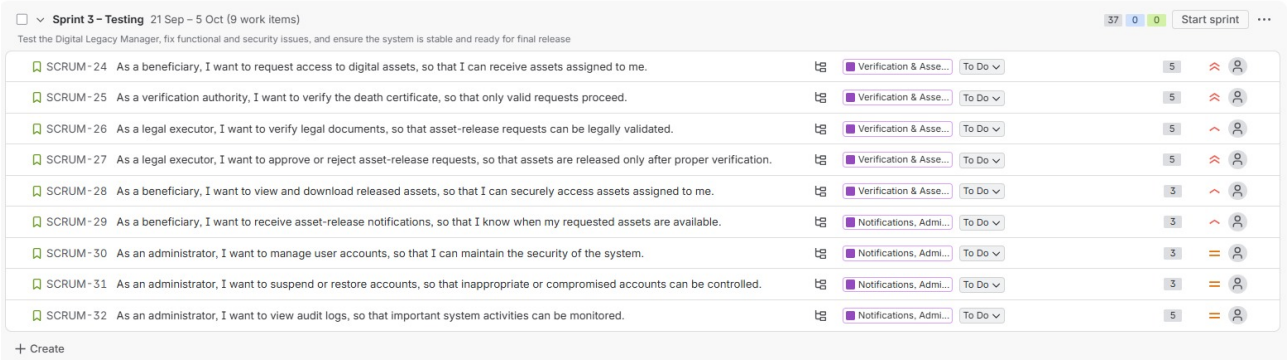


Figure 6. Sprint 3 planning view showing nine work items and the testing goal.

Sprint allocation summary: 21 + 16 + 37 = 74 points across the three displayed Sprints. The remaining 10 points correspond to SCRUM-16 and SCRUM-17, which are outside the displayed Sprint allocation.

5. Versions / Releases

The Jira project includes a **v1.0 MVP** release. The release evidence identifies the intended product boundary and provides a date range for release planning.



Releases

Release	Status	Progress	Start date	Release date	Description	More actions
v1.0 MVP	UNRELEASED	No work items	August 25, 2026	September 30, 2026	Initial MVP release of the Digital Legacy Manager containing secure authentication, digital asset management, digital will and beneficiary management, verification, asset release, notifications, administration, and audit logging.	···

Figure 7. Jira Releases view showing v1.0 MVP, its start date, release date and description.

Release planning observation. The configured release date is **30 September 2026**, while the displayed Sprint 3 ends on **5 October 2026**. If all three Sprints are intended to contribute to v1.0 MVP, the release boundary should be aligned with the Sprint schedule before final execution.

6. Active Scrum Board Workflow & Issue Traceability

The Jira workflow uses the Scrum status sequence **To Do → In Progress → Done**. Sprint 1 provides the clearest evidence of active execution: several authentication and encryption stories are Done while SCRUM-19 is In Progress. Later Sprint views contain planned To Do work.

At the issue level, the project maintains traceability through:

- Parent Epic — identifies the functional module.
- Sprint — identifies the planned iteration.
- Priority — communicates relative importance.
- Labels — provide additional classification such as authentication, digital-assets and security.
- Assignee — provides visible work ownership.
- Subtasks — break a User Story into design, implementation, validation and testing activities.




Figure 8. Example Jira issue metadata and ownership evidence.

7. Sprint Burndown Chart

The Sprint 1 burndown chart compares remaining story points with an ideal burn-rate guideline. It provides a visual way to inspect whether the Sprint is progressing toward zero remaining work by the planned end date.

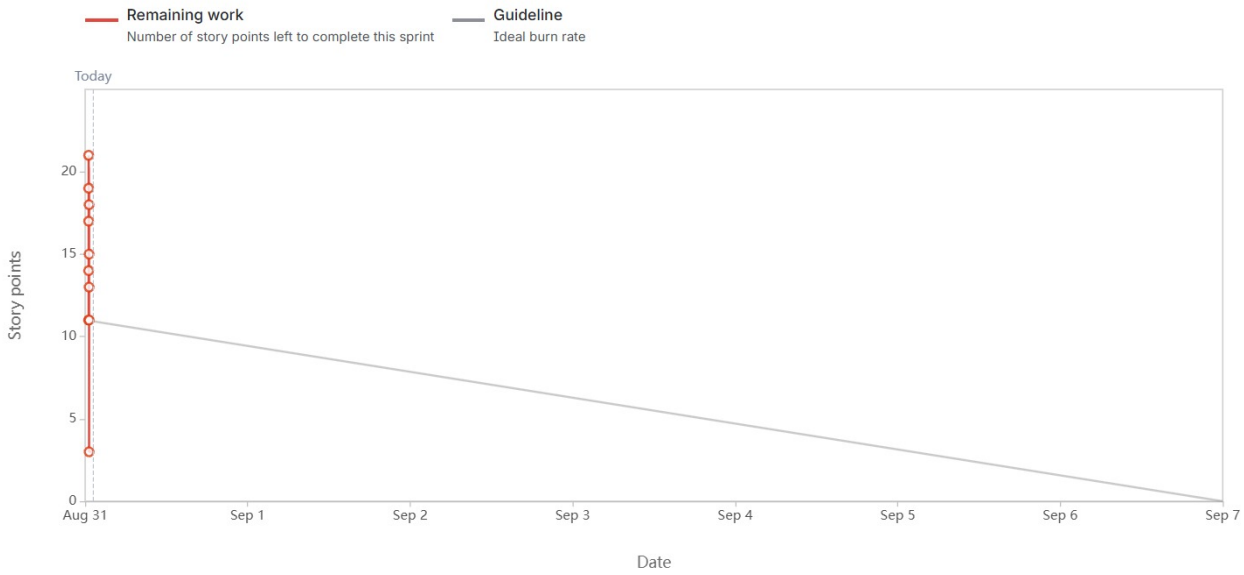


Figure 9. Sprint 1 burndown chart — remaining work versus ideal guideline.

The visible chart contains a steep concentration of remaining work at the start of the Sprint, followed by the ideal guideline toward the Sprint end. Such a chart can be used during Sprint reviews to identify late scope changes, uneven completion or a need to rebalance work.

8. Jira Dashboard & Progress Metrics

The Jira dashboard provides quantitative evidence of project activity. The captured dashboard reports **112 total work items** across the displayed charts, including stories, subtasks, tasks and epics.

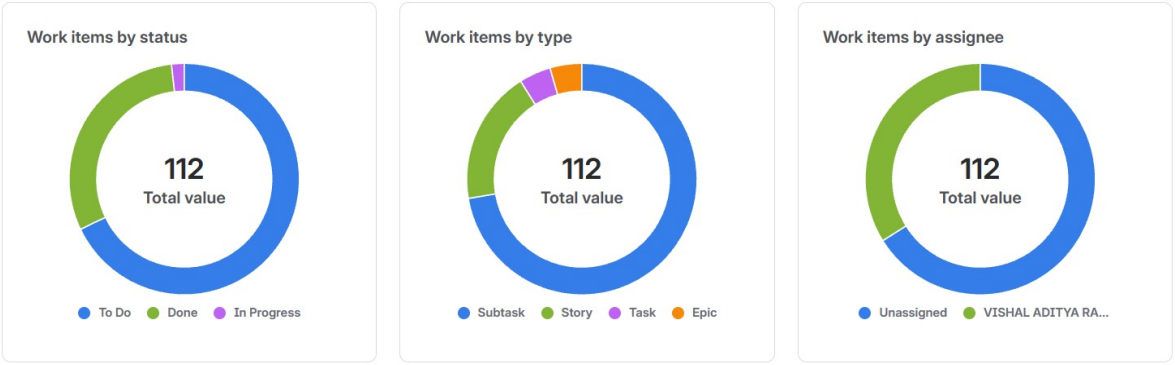


Figure 10. Dashboard status, type and assignee charts.



Figure 11. Dashboard activity cards showing completed, updated, created and due work items.

8.1 Dashboard Trends

The dashboard also provides trend and cycle-time views that can support Scrum inspection and adaptation.

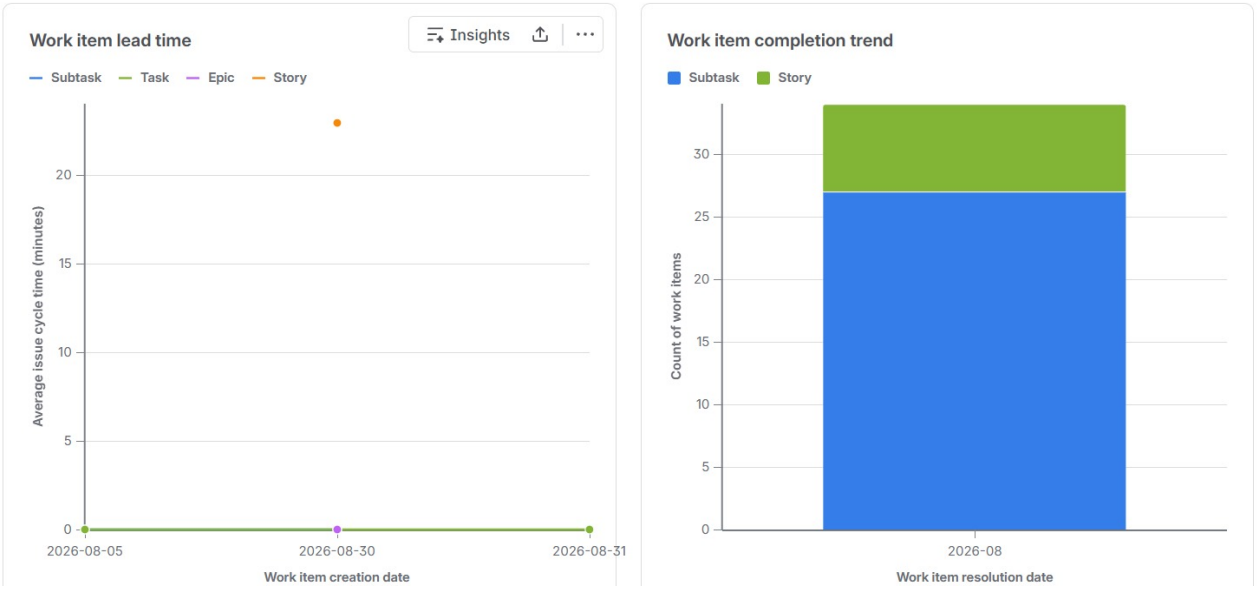


Figure 12. Work-item lead-time and completion-trend charts.

Interpretation. The charts provide a quantitative snapshot of work creation, completion and cycle/lead time. These measures are useful during Sprint reviews and retrospectives because they complement the visual Scrum Board with evidence about throughput and flow.

9. Backlog Grooming & Prioritization

Backlog grooming was represented through structured ordering, Epic relationships, priority levels, labels and story-point estimates. Higher-value security and access functions are positioned earlier because later release operations depend on them.

Examples of logical dependency:

- Users must register and authenticate before securely managing assets.
- Digital assets and a digital will must exist before beneficiary transfer can be requested.
- Death-certificate and legal-document verification should occur before an executor approves release.
- Notifications and audit logging support the release and administrative lifecycle.

Subtasks further refine the backlog. For example, a registration story can be decomposed into interface design, form implementation, validation, password security and testing, while executor approval can be separated into interface, verification-result display, approval, rejection and testing.

10. Sprint Retrospective

What went well

- Five coherent Epics and 21 User Stories provide a manageable structure for a security-sensitive system.
- User Stories contain explicit acceptance criteria and are decomposed into implementation/testing subtasks.
- Jira makes ownership, priority, labels, story points, Sprint assignment and status visible.
- The three-Sprint progression moves from core access/assets to digital-will enhancements and finally verification/release/administration.

Challenges encountered

- SCRUM-16 and SCRUM-17 remain outside the displayed Sprint allocation and should be reviewed.
- Sprint 2 and Sprint 3 contain planned To Do work, indicating that significant functionality is not yet complete in the captured state.
- The release boundary and Sprint 3 end date are currently misaligned.
- Security-sensitive verification, authorization and audit dependencies require careful sequencing and ownership.

11. Areas for Improvement

- Finalize Sprint allocation for every backlog story before locking the release plan.
- Align the v1.0 MVP release date with the final Sprint schedule.
- Continue assigning subtasks to named owners instead of leaving implementation work unassigned.
- Review burndown and dashboard metrics during every Sprint review to identify scope or progress issues early.
- Use backlog grooming to revisit dependencies and priorities as Sprint execution produces new information.
- Maintain consistent acceptance criteria and testing evidence for security- and verification-related stories.

12. How Scrum Practices Helped

Epics grouped related capabilities into meaningful modules. User Stories represented requirements from the perspectives of users, beneficiaries, verification authorities, legal executors and administrators. Subtasks converted those requirements into actionable design, implementation and testing activities.

Sprint planning created time-bounded increments with explicit goals and point estimates. The Scrum Board made To Do, In Progress and Done work visible, while priorities and labels improved organization. Release planning connected the backlog to a target MVP. Burndown and dashboard metrics provided quantitative evidence for progress monitoring, and the retrospective created a structured mechanism for continuous improvement.

13. Final Project Summary

Digital Legacy Manager is a secure digital-legacy platform designed to organize, protect and transfer digital assets to authorized beneficiaries. The Jira Scrum implementation translates the project into five functional Epics, 21 User Stories and a substantial set of implementation/testing subtasks.

The backlog contains **84 story points**. Three displayed Sprints account for **74 points**: Sprint 1 – Digital Legacy MVP (21), Sprint 2 – Enhancements (16), and Sprint 3 – Testing (37). The remaining 10 points are represented by SCRUM-16 and SCRUM-17 outside the displayed Sprint allocation.

Overall, the evidence demonstrates Product Backlog organization, Epic-to-Story relationships, acceptance criteria, story points, labels, assignees, Sprint planning, Scrum-board status tracking, release planning, dashboard metrics, burndown analysis, backlog grooming and retrospective practice.

Conclusion. The Jira implementation provides an inspectable Scrum framework for managing a security-sensitive Digital Legacy Manager. It connects requirements to implementation through Epics, User Stories and subtasks, then organizes the work into Sprints and a planned MVP release. The captured evidence also highlights realistic planning issues, giving the team clear opportunities for improvement before final execution.

Appendix A — Evidence Index

Figure	Evidence	What it demonstrates
1	Epic panel	Five project Epics and their functional grouping.
2	Issue details	Assignee, Parent Epic, Sprint, Priority and Label traceability.
3	Product Backlog	21 User Stories with Epic relationships, priorities and story points.
4	Sprint 1	Six work items and visible Done/In Progress status evidence.
5	Sprint 2	Four digital-will/beneficiary stories and Sprint goal.
6	Sprint 3	Nine verification/release/administration/testing stories.
7	Release view	v1.0 MVP release dates and description.
8	Issue metadata	Example of ownership and issue-level Scrum traceability.
9	Burndown	Remaining Sprint 1 work versus ideal burn-rate guideline.
10	Dashboard charts	Work items by status, type and assignee.
11	Dashboard cards	Recent completed, updated, created and due work.
12	Dashboard trends	Lead-time and completion-trend evidence.
13+	User-story screenshots	Acceptance criteria and subtask decomposition for SCRUM-12 through SCRUM-32.

Submission checklist

✓ Five Epics represented in Jira

✓ 21 User Stories with Scrum-format descriptions

✓ Acceptance criteria and implementation/testing subtasks

✓ Story points and priorities visible

✓ Three Sprints with goals and dates

✓ Scrum-board status evidence

✓ Labels, assignees and issue traceability

✓ v1.0 MVP release evidence

✓ Dashboard and burndown evidence

✓ Backlog grooming, retrospective and improvement analysis

Jira project: bharathkumar13.atlassian.net/jira/software/projects/SCRUM/boards/1/backlog
